

Measure Q Bond Program Overall Program Update


As of October 13, 2025

Program Funding Sources



| Funding source | Funding amount ① |
|---|------------------|
| <u> </u> | \$362,108,231 |
| | \$979,005 |
| n Physical Plant/Instructional Support (PPIS) 22-23 | \$2,569,568 |
| ⚠ Prop 39 Clean Energy | \$712,447 |
| | \$1,029,582 |
| ☐ Solano Transportation Authority | \$50,000 |
| | \$850,000 |
| | \$33,451,000 |
| | \$59,145 |
| Total | \$401,808,978 |

Budget by Categories



| Budget group | Budget |
|---|---------------|
| Site Acquisition | \$15,024,659 |
| ■ Plans | \$7,562,598 |
| Working Drawings | \$13,847,424 |
| ■ Construction | \$231,605,999 |
| ■ Contingency | \$41,697,366 |
| Architectural and Engineering Oversight | \$55,693,632 |
| ■ Tests and Inspections | \$4,214,264 |
| ■ Construction Management | \$6,580,800 |
| Furniture and Group II Equipment | \$23,358,374 |
| ■ COVID | \$188,077 |
| Unallocated Interest | \$8,110,891 |
| Total | \$407,884,085 |

Expense by Categories




| Budget group | Budget |
|---|---------------|
| Site Acquisition | \$15,024,659 |
| ■ Plans | \$7,562,598 |
| ■ Working Drawings | \$13,847,424 |
| ■ Construction | \$231,605,999 |
| ■ Contingency | \$41,697,366 |
| Architectural and Engineering Oversight | \$55,693,632 |
| ■ Tests and Inspections | \$4,214,264 |
| ■ Construction Management | \$6,580,800 |
| Furniture and Group II Equipment | \$23,358,374 |
| ■ COVID | \$188,077 |
| ■ Unallocated Interest | \$8,110,891 |
| Total | \$407,884,085 |



Measure Q Bond Program Overall Program Update

As of October 13, 2025

Budget Status and Budget vs Expenditures and Encumbrances

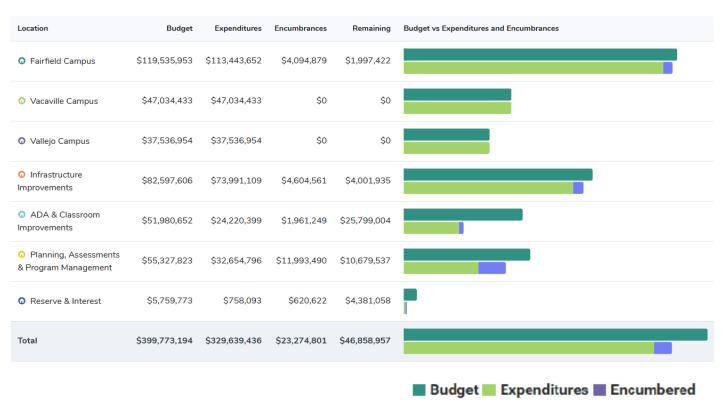

Expenditures by Location (total expenditures by fiscal year)

